






- **R** OOSEVELT
  - NNOVATION
- **D** ESIGN
- **E** NGINEERING
- **R** ESEARCH

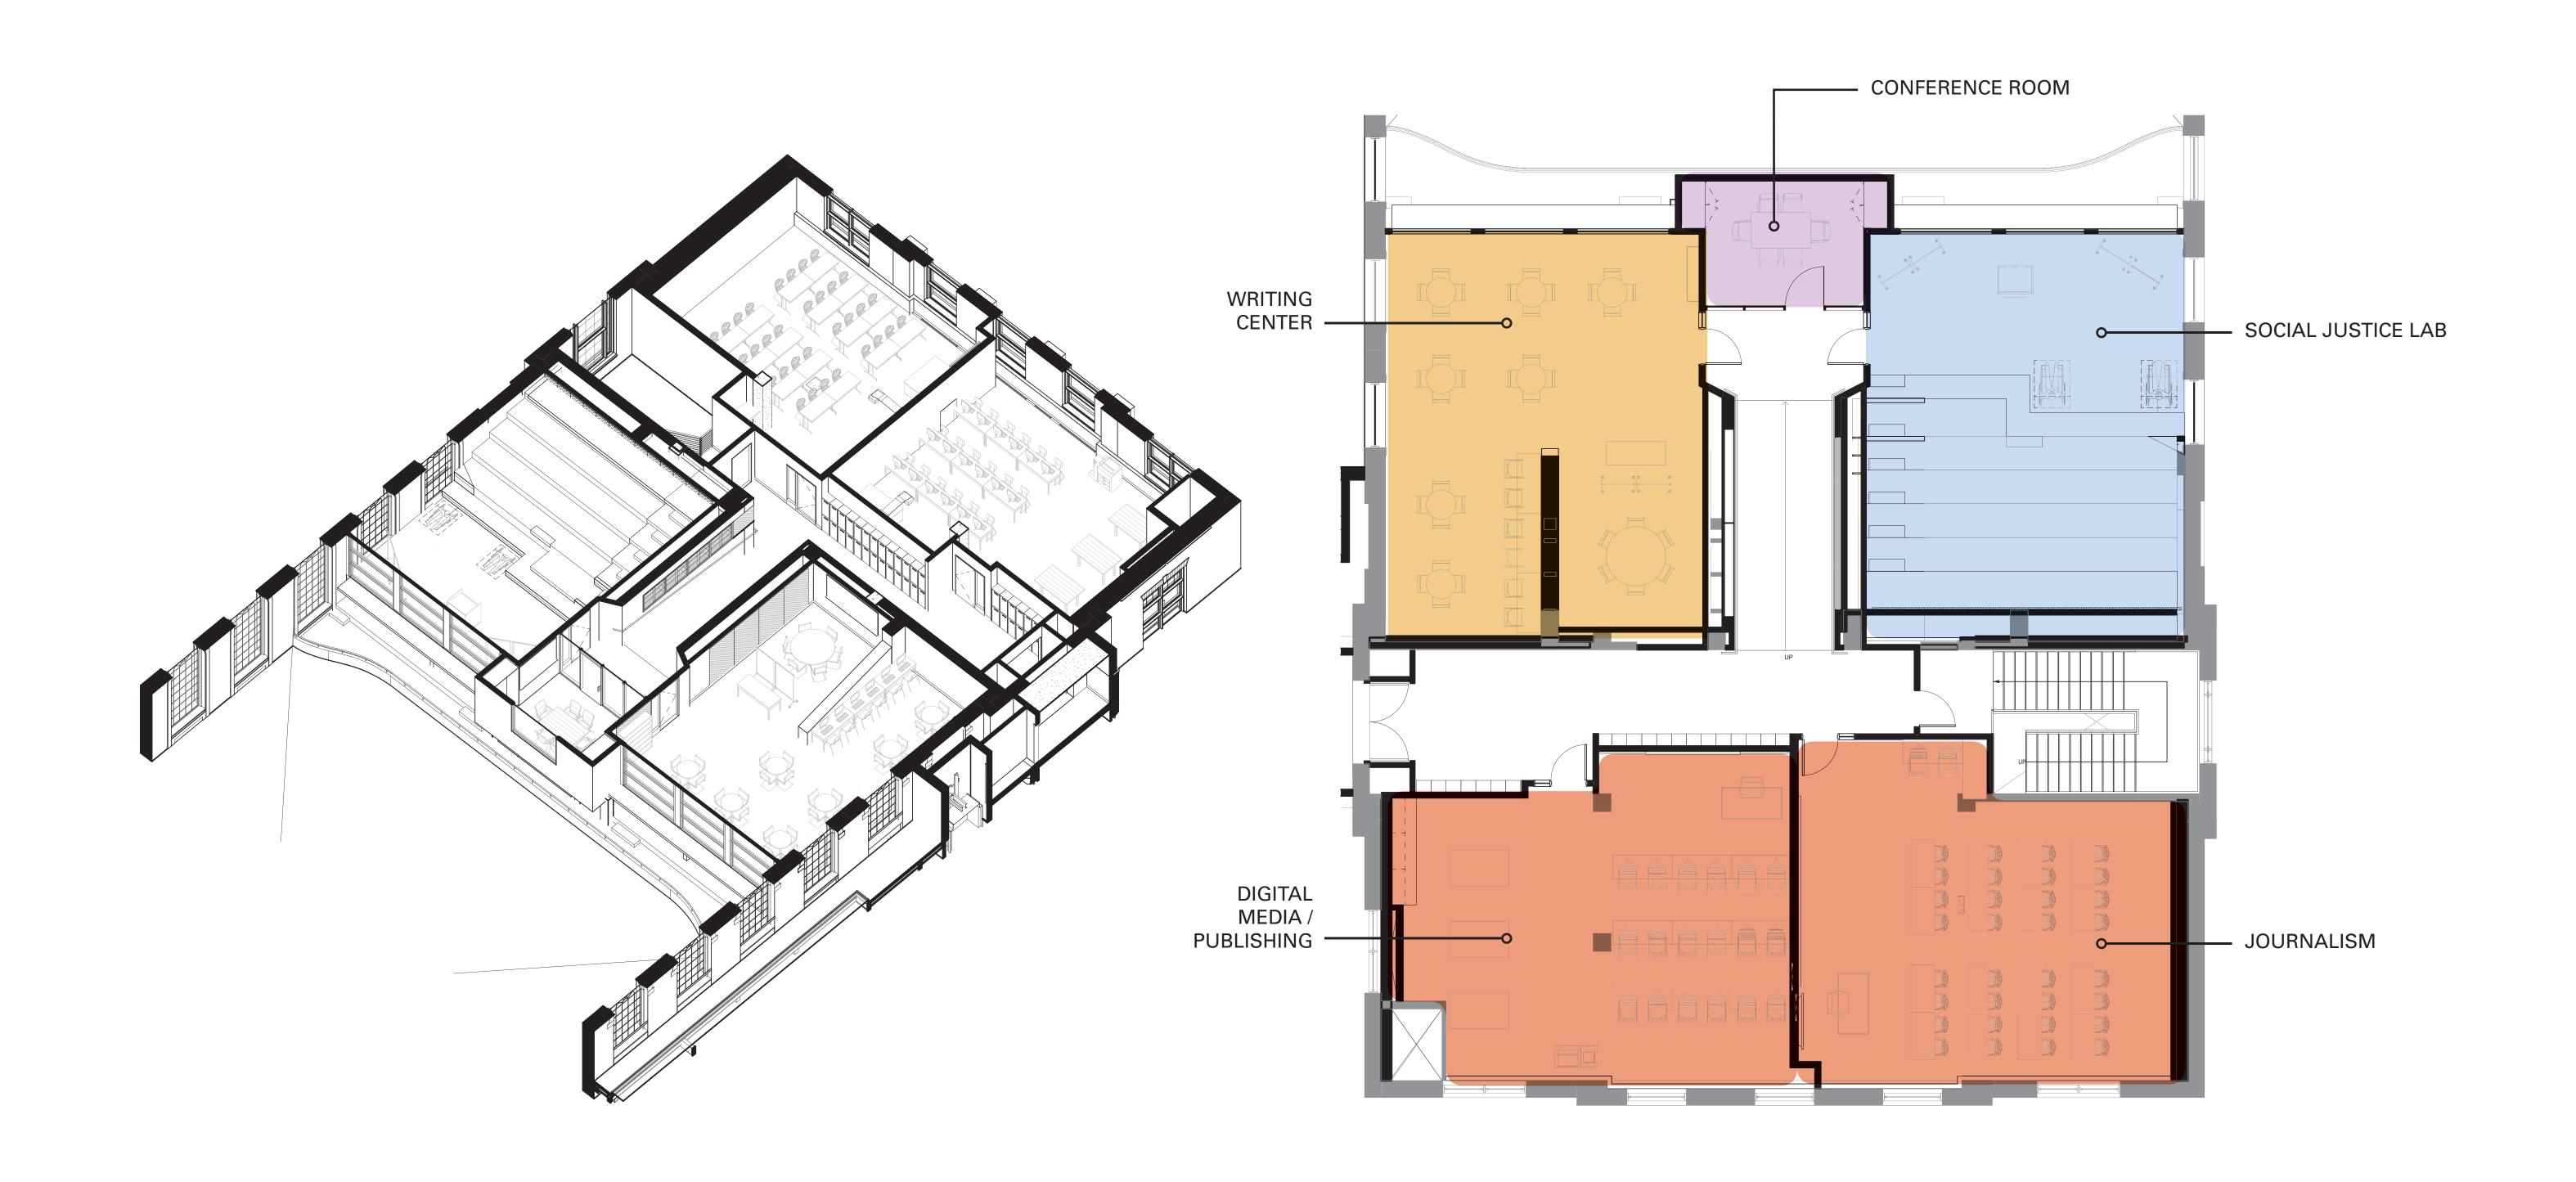

0 2' 4'

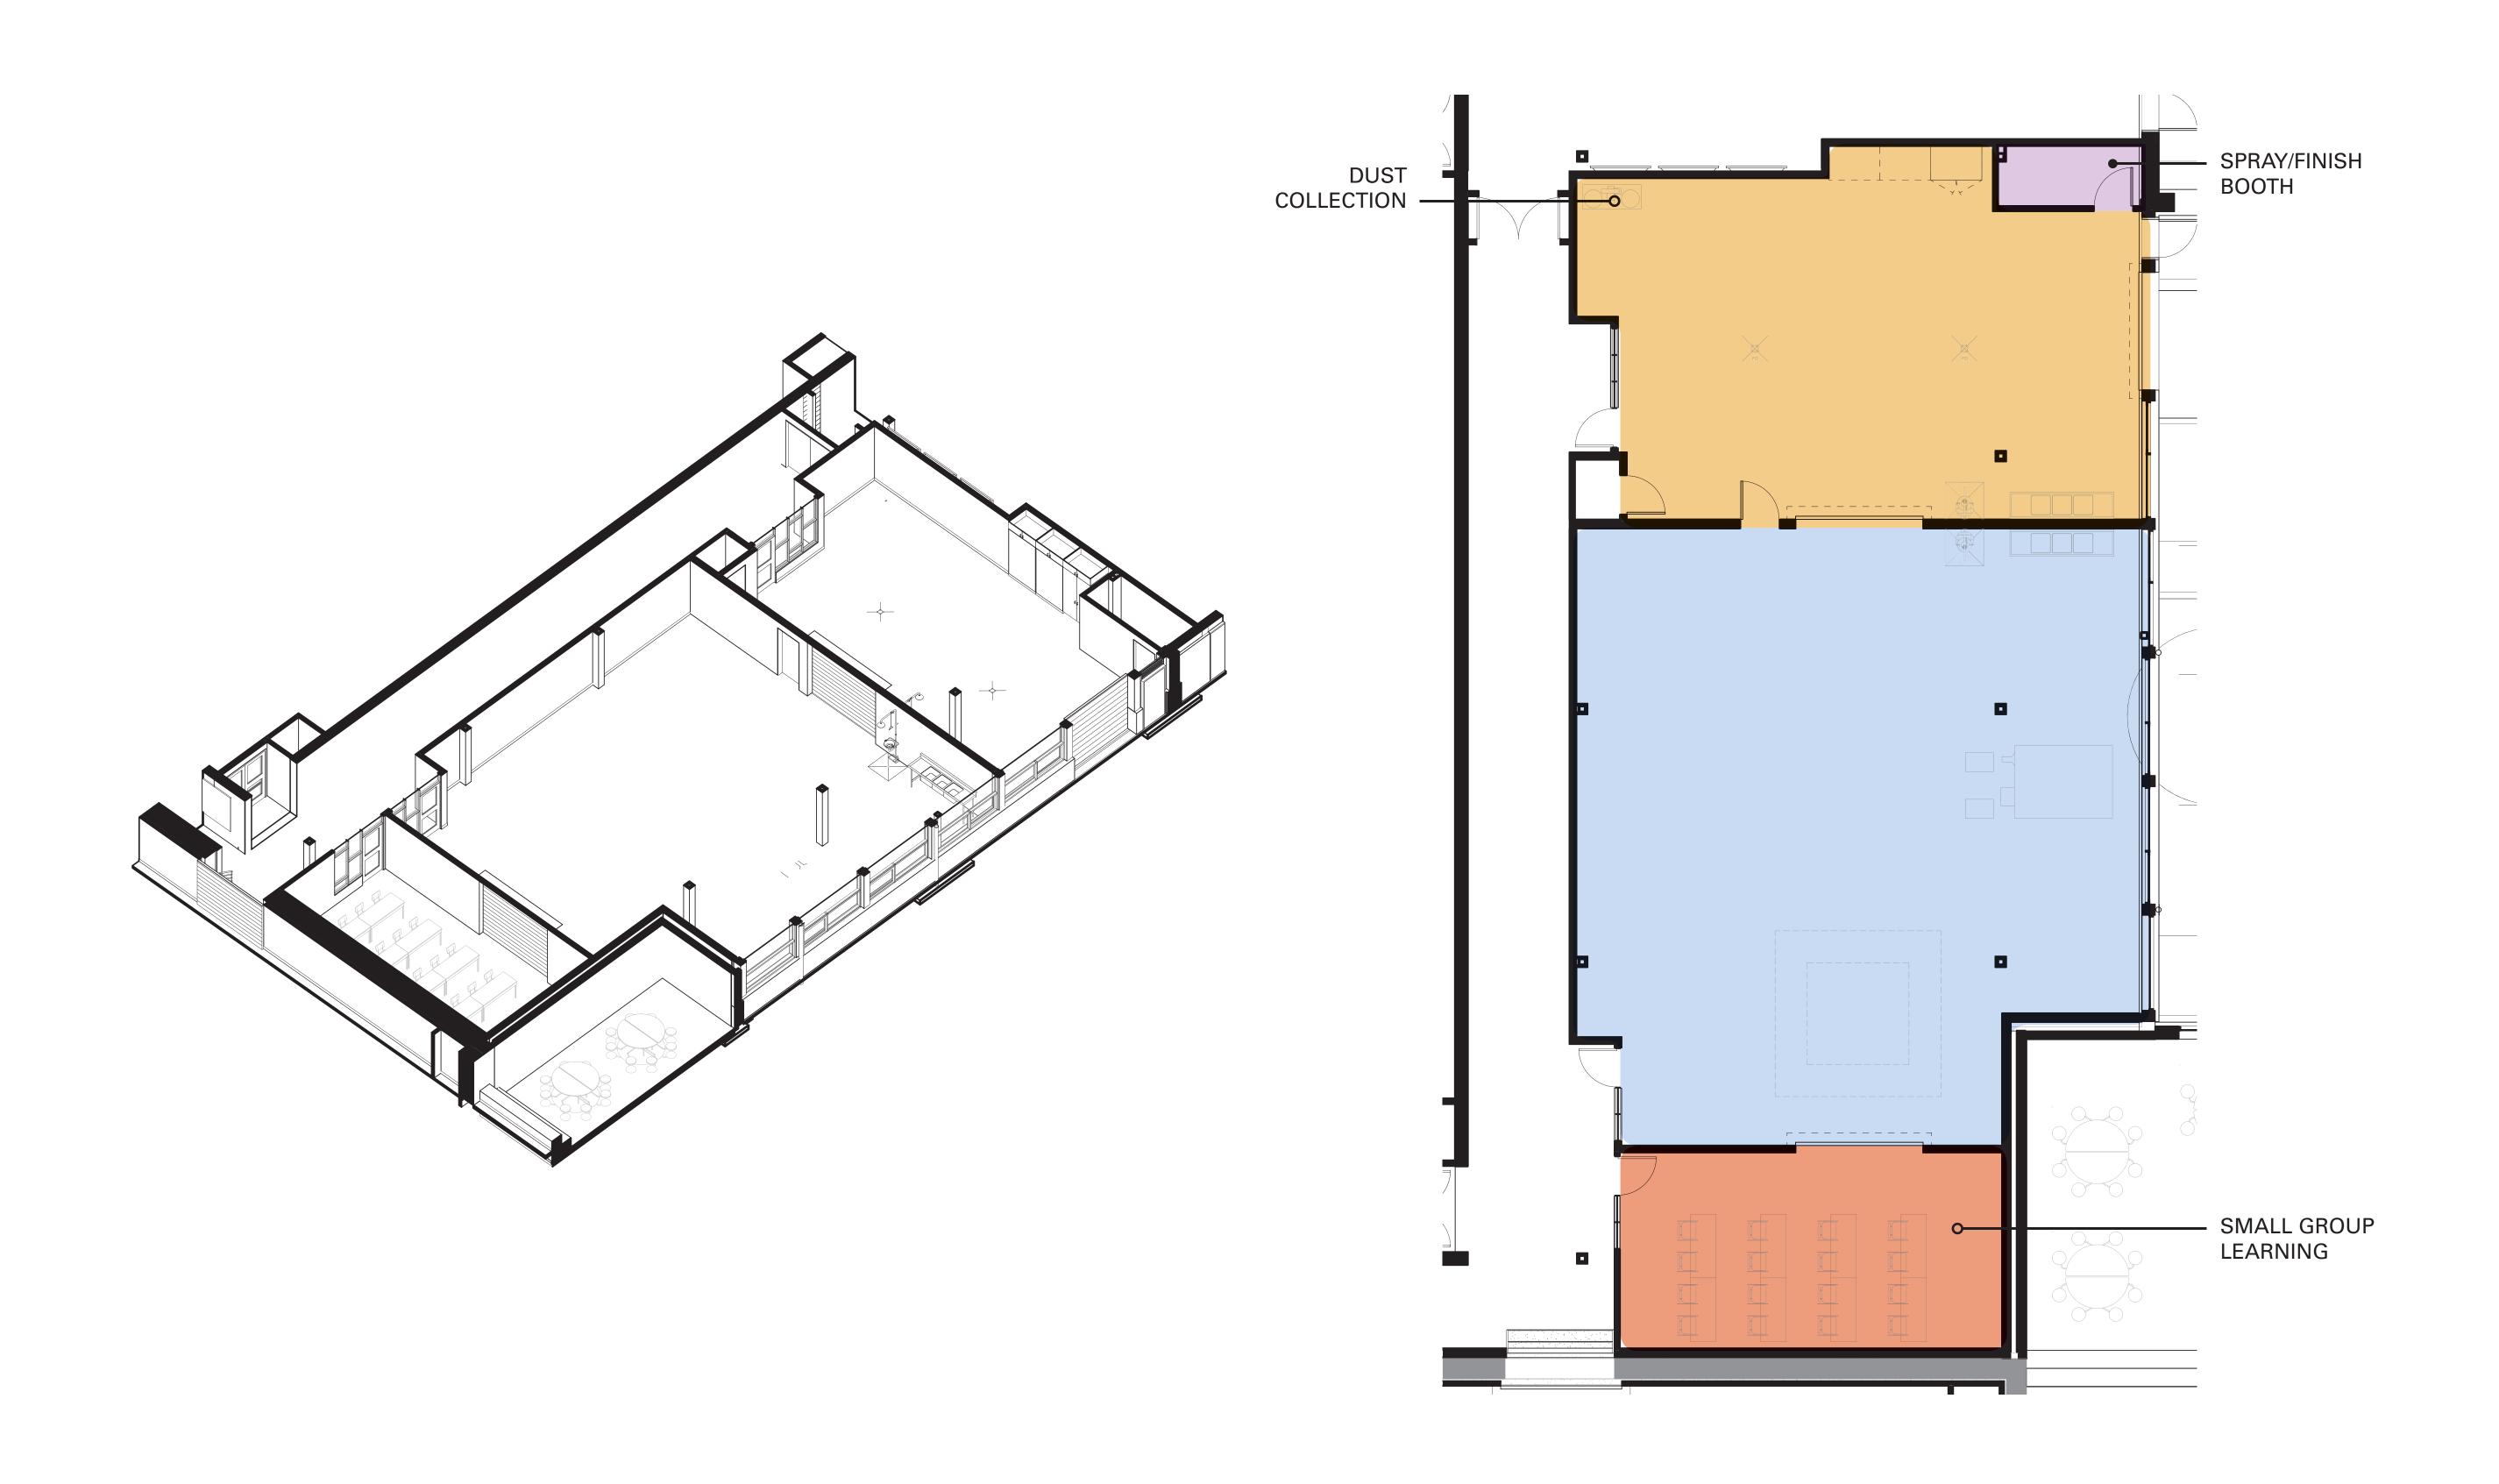

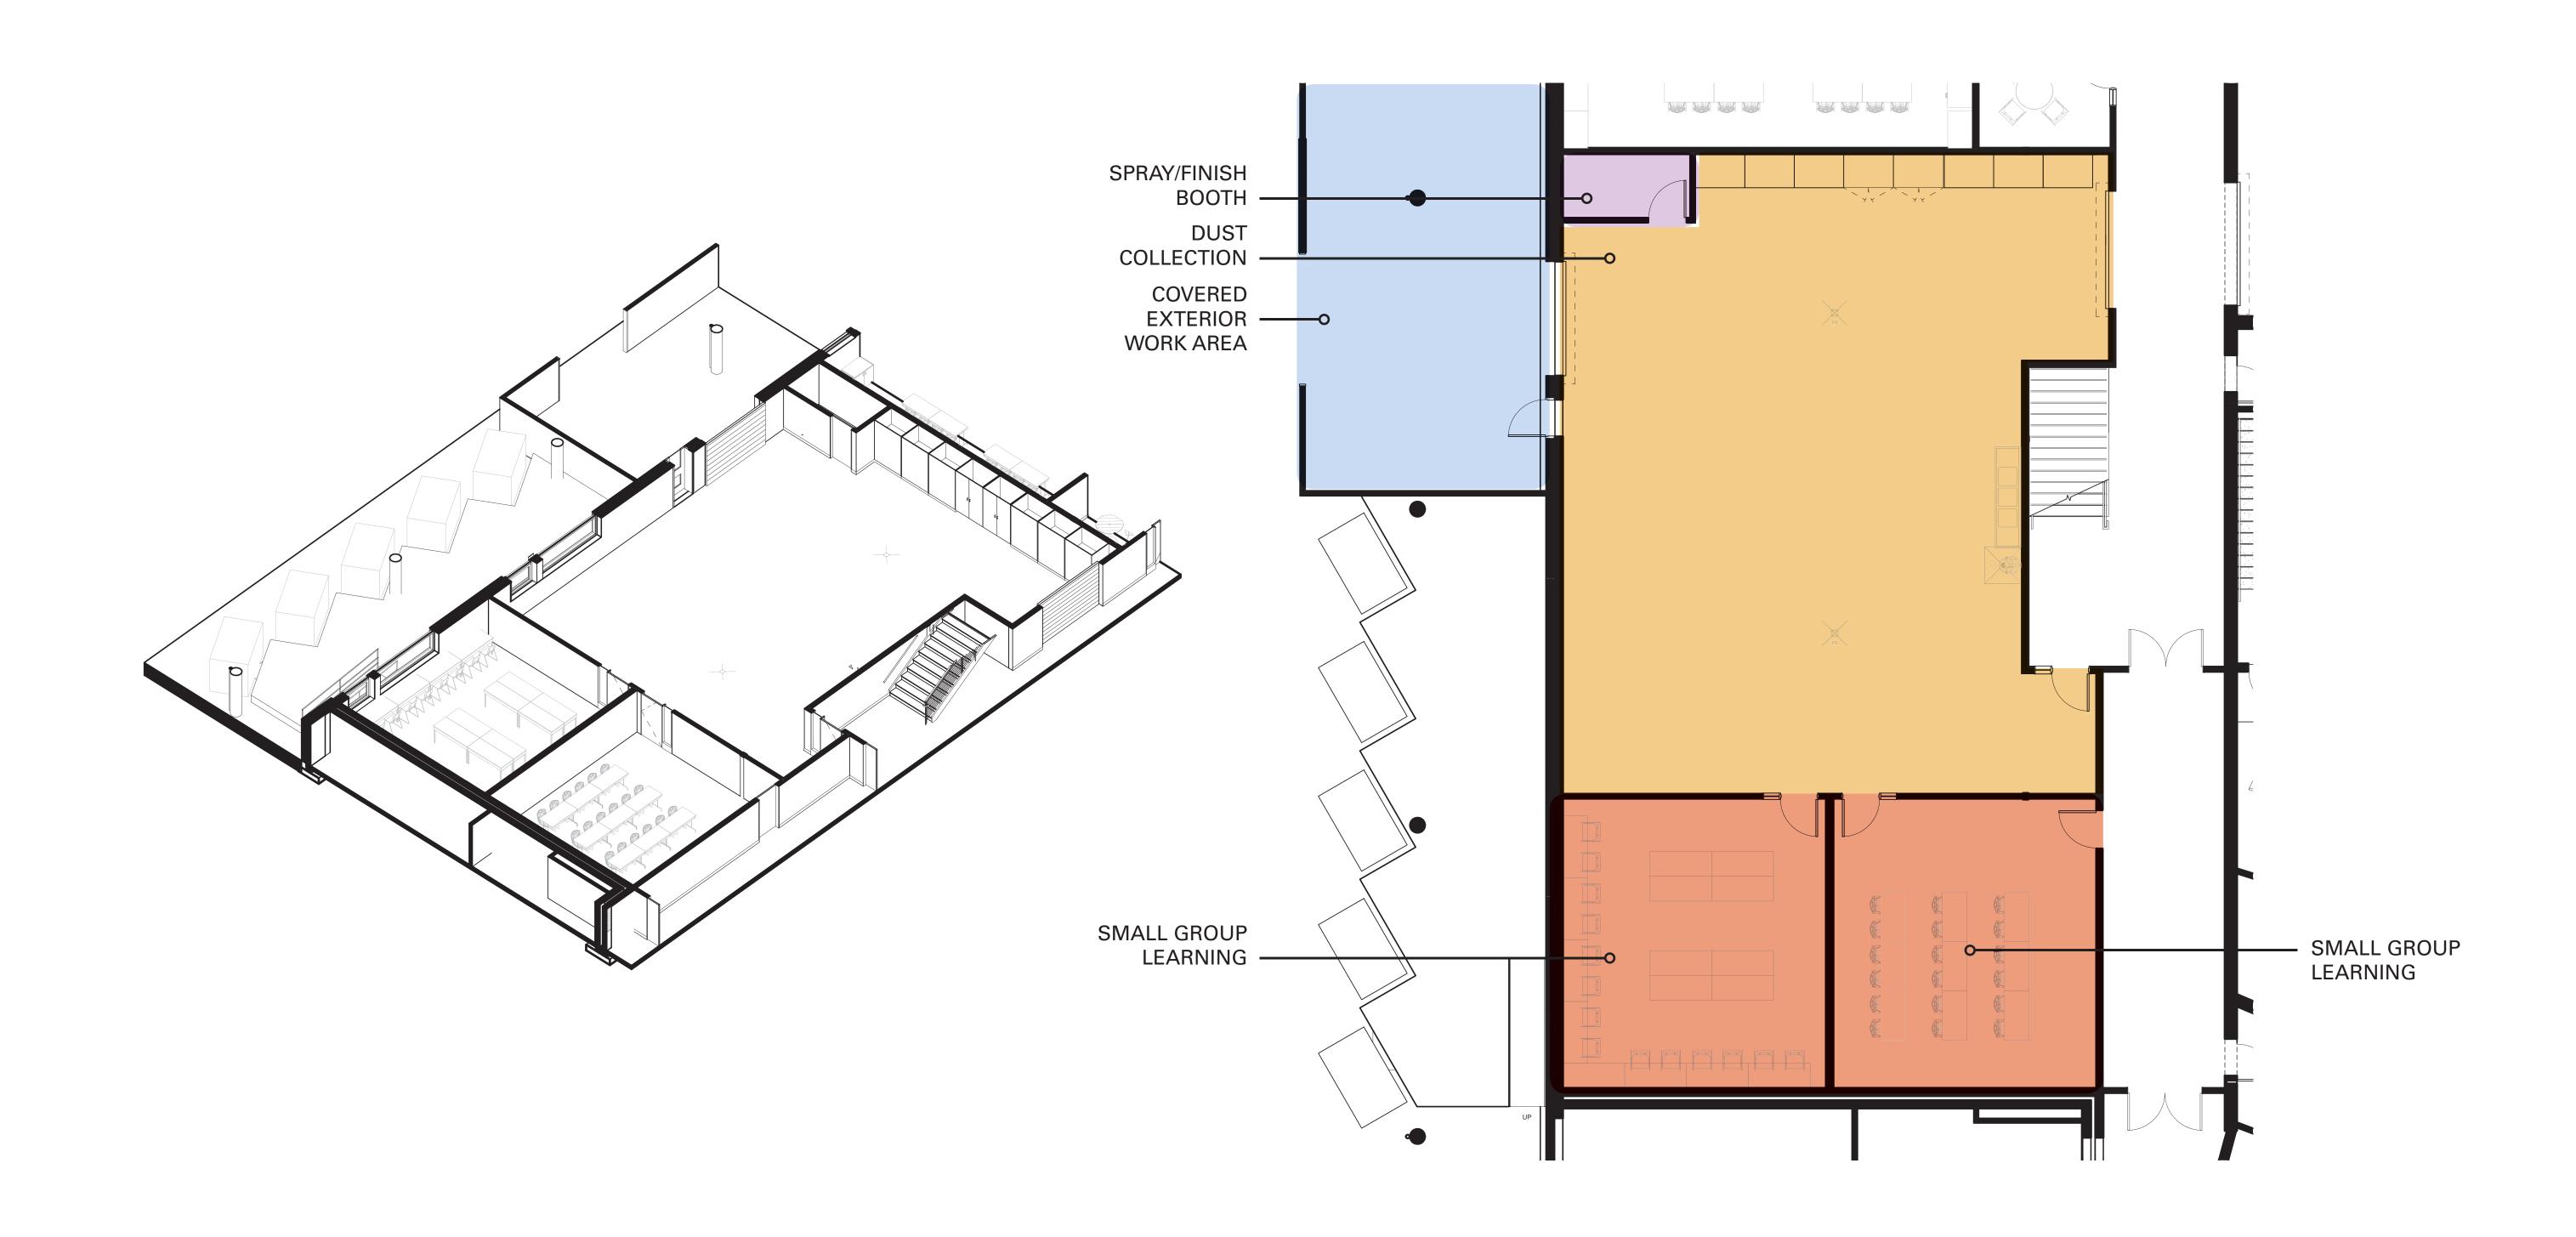



### PHASES

- Preconstruction (Spring 2015)
- Phase I (Spring 2015-Summer 2016)
  - New construction on gymnasium, theater, commons/cafeteria, classroom wings, career pathway spaces & library conversion
- Phase II (Summer 2016-Summer 2017)
  - Renovation of main building including offices, classrooms, rest of commons/cafeteria
- Phase III (Summer 2017-Winter 2017)
  - Final demolition of buildings and sitework


**TIMELINE** | Phases (Summers)

PHASE II PHASE III PHASE III

# **SPRING 2015 – SUMMER 2015**

- Contactor sets up in shops
- Fences go up
- Gymnasium, music bldg, boiler demolished
- Temporary facilities constructed
- New construction begins
- Renovation begins


**TIMELINE** | Pre-Construction

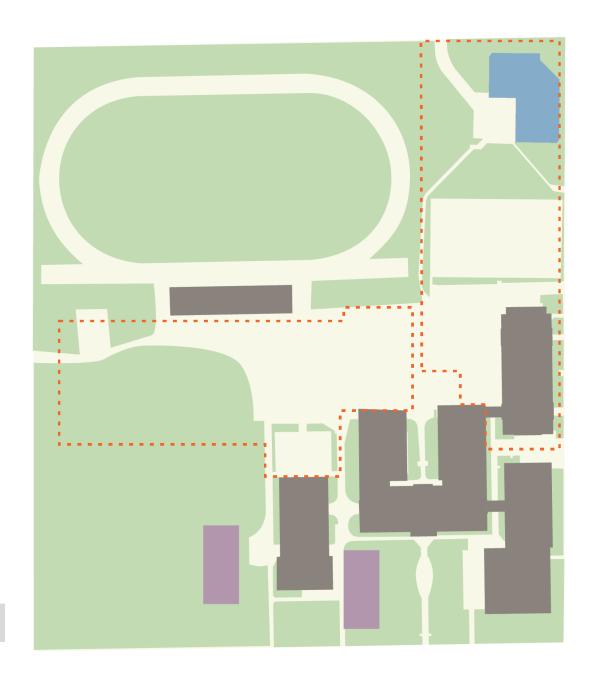

#### 2015 - 2016 SCHOOL YEAR

- Contactor on-site
- Construction fence up throughout school year
- Temporary facilities open
- Construction proceeds on gymnasium, new auditorium
- Auditorium → library renovation begins


**TIMELINE** | Phase I

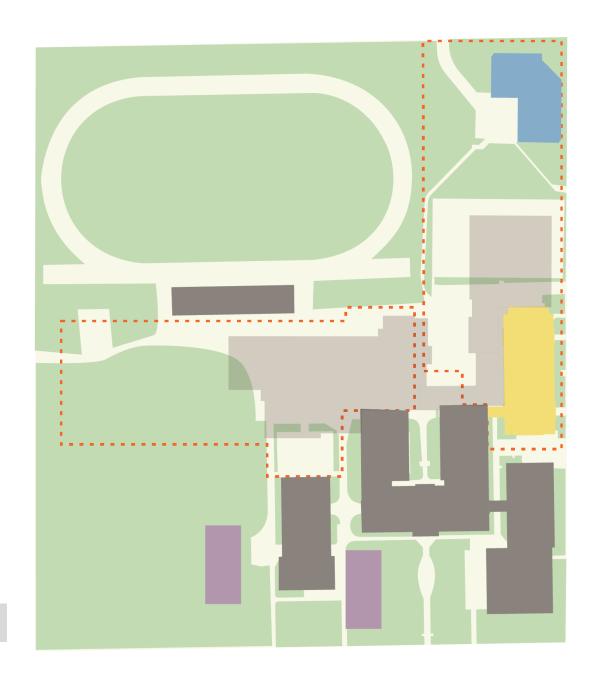

#### 2016 –2017 SCHOOL YEAR

- Contractor remains in shops
- Construction fence moves
- New auditorium & gym wings open
- Temporary facilities remain
- Construction proceeds on second half of commons
- Renovations in 1921 building begin

TIMELINE | Phase II

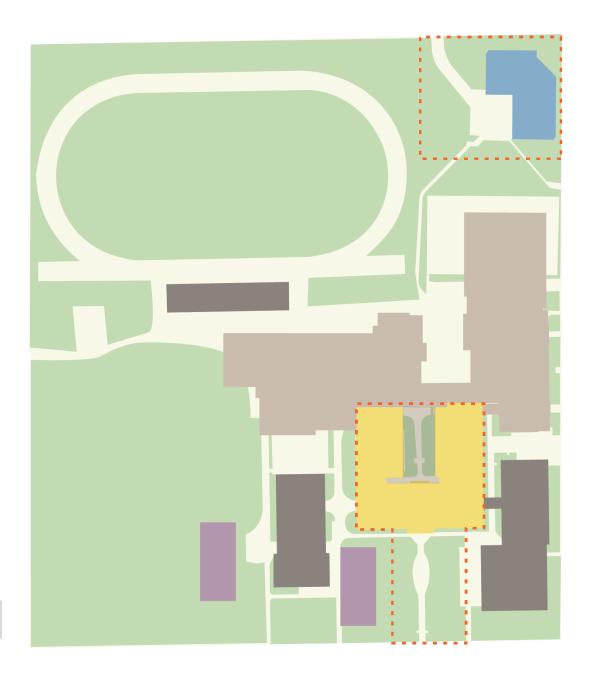

## **SUMMER 2017 –** WINTER 2017

- Shops, library, cafeteria wings demolished
- Construction fence removed
- Temporary facilities removed
- Rest of new commons opens
- Building work is complete
- Site work and landscaping occurs

TIMELINE | Phase III

